STATE	PROJ. NO.	SHEET NO.	TOTAL SHEETS
N. H.			

CONSTRUCTION SIGNS AND WARNING DEVICES		
TYPE	CODE	NO. REQ'D.
Permanent Signs	W20-1a	6
	W20-1d	9
	G20-2	6
Operational Controls	W20-5	12 6Lt. 6Rt.
	W20-5a	12 6Lt. 6Rt.
	W20-9	6
	#BARRICADE WARNING LIGHTS TYPE "A" OR "C"	6
	EASELS	24
	*SIGN PADDLES	3
	36" BLAZE ORANGE TRAFFIC CONES	54
	OM-1	18

Warning Lights shall be Type "A" or Type "C" at the discretion of the Engineer as delineated in paragraph 6D-5 of the M.U.T.C.D.

*STOP/SLOW paddles shall be fabricated as described in paragraph 6E-2 in the M.U.T.C.D. Handle to be provided.

3 Each Hall-Kirby Sentinel arrow board trailers (or equal) (To be located as directed by the Engineer)

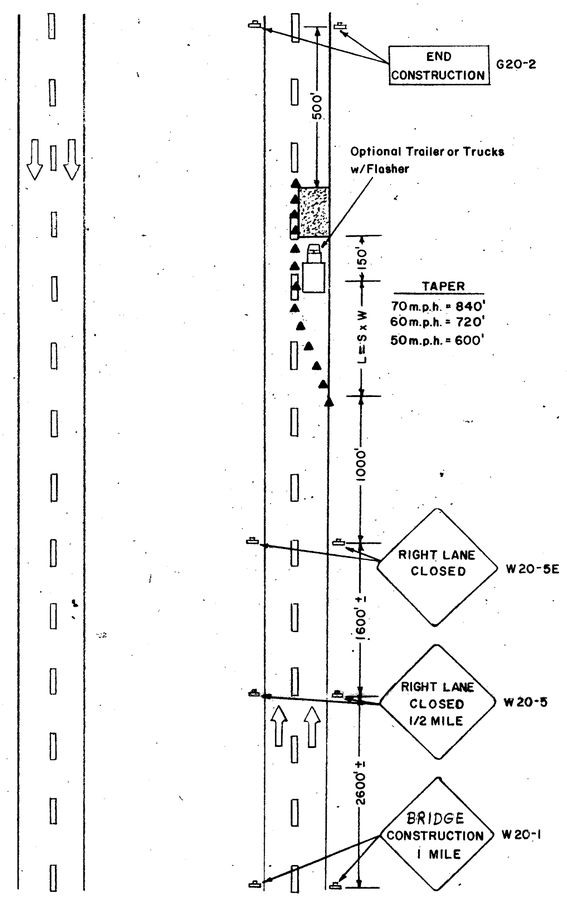

Lane closure — 4-lane divided roadway where half of roadway is closed.

NOTE:

L = Length of Taper

S = Numerical Value of the Speed Limit

W = Width of offset in feet

KEY:

▲ 36" Ballasted Cones at minimum 50' Spacing

LEFT LANE CLOSURE IN KIND

NOTE: Materials and fabrication shall conform to SIGN STANDARD SHEETS CS-1 & CS-2 and SECTION 619 of the STANDARD SPECIFICATIONS.

W20-9 (OPTIONAL USE)

SALEM - WINDHAM
BR. NO's.-SALEM 068/078, 058/088, WINDHAM 139/094, 135/090, 137/101
STATE PROJECT: P-2708-B

EXPANSION JOINT RECONSTRUCTION OF I-93 BRIDGES

CONSTRUCTION SIGNS AND WARNING DEVICES LAYOUT

~~33-4-3~~

13-3-2

PROJ. NO.	SHEET NO.	TOTAL SHEETS
P-2708-B	14	14

REVISIONS AFTER PROPOSAL (USE BOTTOM LINES FIRST)				
NO.	DATE	STATION	STATION	DESCRIPTION

NOTEBOOKS			
BOOK NO.	PAGE NO.	BOOK NO.	PAGE NO.
" "	" "	" "	" "

		DATE
PLAN TRACED	D. Nelson	2/1/72
PLAN CHECKED	A. HARRISON	2/2/72
PROFILE TRACED		
PROFILE CHECKED		
INKED		
CHECKED		
